

December 8, 2020

Mr. Vernal Sibble, P.E, Project Manager
City of Hollywood Public Utilities Department
1621 North 14th Avenue
Hollywood, Florida 33022

**RE: LIFT STATION W-14 UPGRADE
PROJECT NO.: 17-8063
Proposed Change Order No. 2:
CONTRACTOR'S TIME EXTENSION REQUEST**

Dear Mr. Sibble:

We have reviewed the project schedule and the Contractor's request for the time extension without any change in Contract Price due to the delays in getting the electrical control equipment for the project. We recommend a total of 238 days extension including 30 day time for certification by EPD and 11 day contingency as shown below and in the attached marked up project schedule.

<u>Contract</u>	<u>Date</u>		
NTP	9/17/2019		
Subst. completion	4/14/2020	210	
Final Completion	6/13/2020	270	
<u>Change Order:1</u>			
Subst. completion	7/13/2020	300	90
Final Completion	9/11/2020	360	90
<u>Proposed Change Order: 2</u>			
VFD shop dwg submittal	10/16/2020		
VFD Reviewed	11/14/2020	29	
delivey of MCC	2/17/2021	95	
Substa. compl	4/7/2021	49	
Final compl	4/26/2021	19	
Substantial Completion days Increased by		268	days
Final Completion Days Increased by		227	days
Total Contract Time		587	days
<u>Contingency</u>			11 days
Final Completion including Contingency	5/7/2021		
Final Completion Days Increased by		238	days

Sincerely,
CRAVEN THOMPSON & ASSOCIATES, INC.



PHILIP JOSEPH, P.E.
Senior Engineer

CRAVEN THOMPSON



& ASSOCIATES INC.

Engineers
Planners
Surveyors
Landscape Architects

3563 N.W. 53rd Street
Fort Lauderdale, FL 33309-6311
(954)739-6400
Fax (954) 739-6409




Project: Hollywood W14 Draft Schedule
Date: Tue 10/13/20

Task
Split
Milestone
Summary




Project Summary
Inactive Task
Inactive Milestone
Inactive Summary



Manual Task
Duration-only
Manual Summary Rollup
Manual Summary




Start-only
Finish-only
External Tasks
External Milestone



Deadline
Progress
Manual Progress



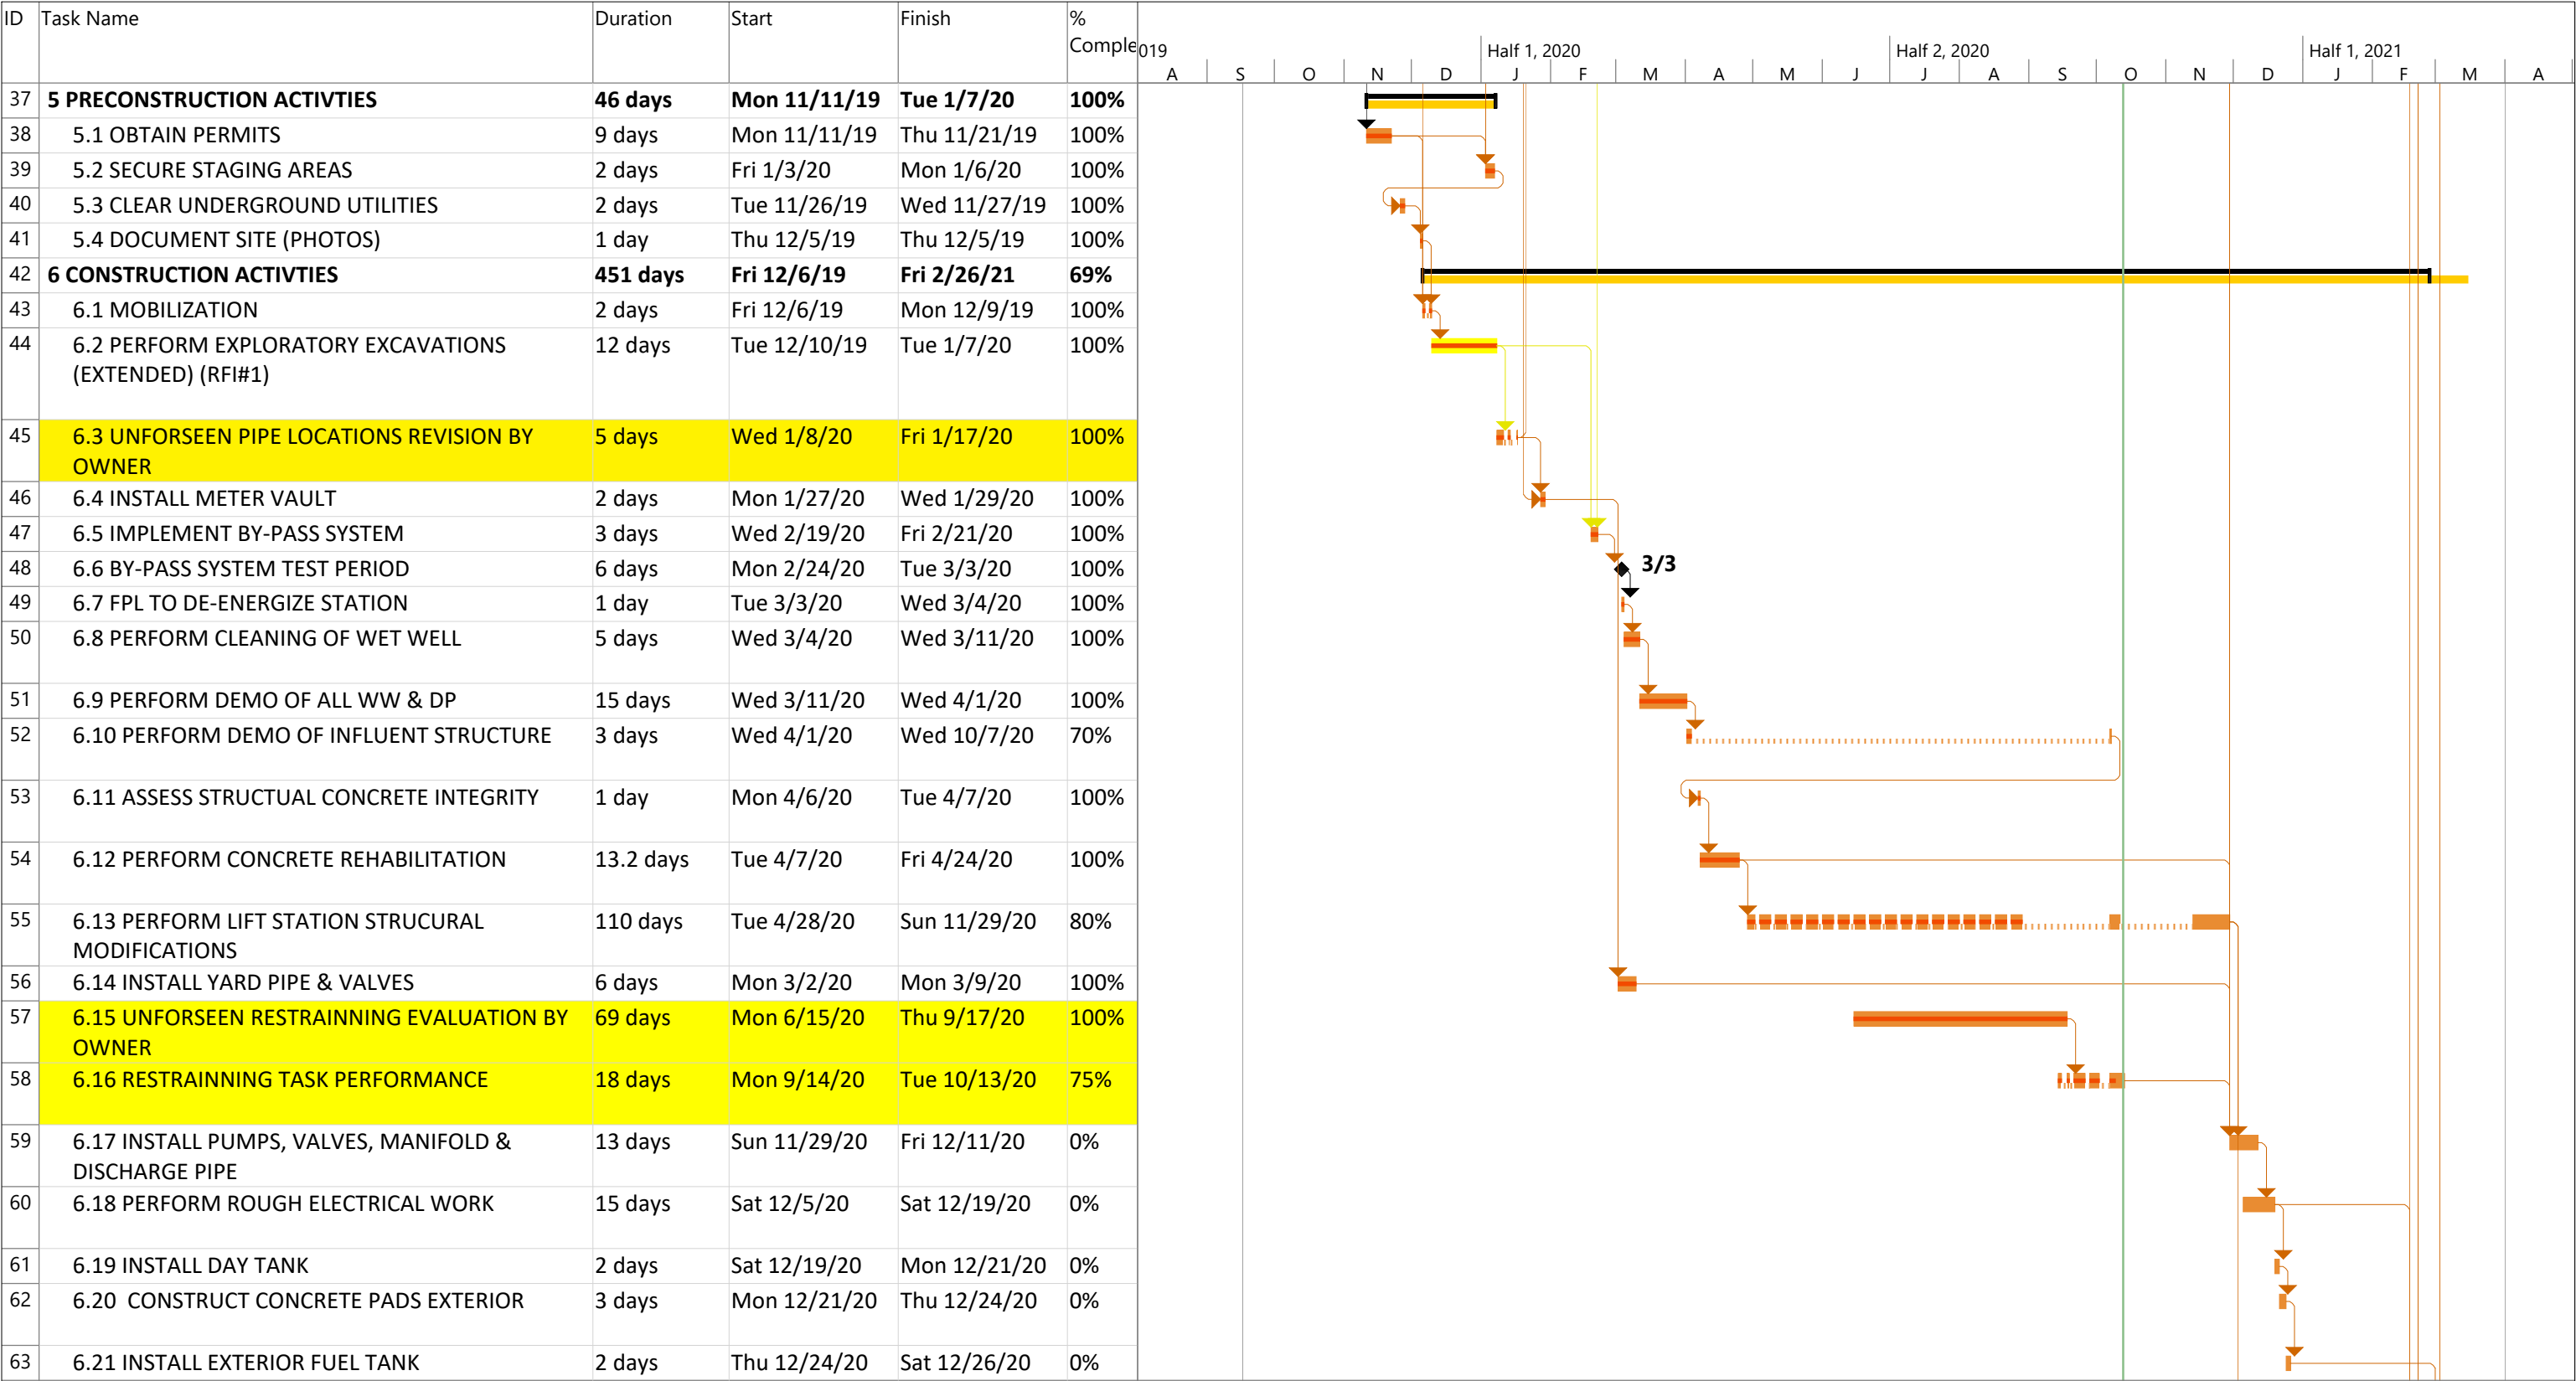

Project: Hollywood W14 Draft Schedule
Date: Tue 10/13/20

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 2

ID	Task Name	Duration	Start	Finish	% Complete																												
						2019					Half 1, 2020						Half 2, 2020						Half 1, 2021										
						A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A							
64	6.22 INSTALL SYSTEM CONTROLS	5 days	Wed 2/17/21	Mon 2/22/21	0%																												
65	6.23 INSTALL ROOF VENTS	21 days	Sun 11/29/20	Sat 12/19/20	0%																												
66	6.24 FINALIZE ELECTRICAL	3 days	Mon 2/22/21	Thu 2/25/21	0%																												
67	6.25 OBTAIN FPL METER	4 days	Thu 2/25/21	Sun 2/28/21	0%																												
68	6.26 PERFORM INTERNAL SYSTEMS TESTING	2 days	Mon 3/1/21	Tue 3/2/21	0%																												
69	6.27 INSTALL GENERATOR	2 days	Wed 3/3/21	Thu 3/4/21	0%																												
70	6.28 PERFORM OFFICIAL SYSTEMS TESTING	2 days	Sat 3/6/21	Sun 3/7/21	0%																												
71	6.29 SUBMIT ASBUILT & TEST RESULT FOR CERTIFICATION	1 day	Sun 3/7/21	Mon 3/8/21	0%																												
72	6.30 EOR TO OBTAIN CERTIFICATION	7 days	Mon 3/8/21	Mon 3/15/21	0%																												
73	6.31 PERFORM SITE RESTORATION, GRADING, SIDEWALK, NEW PAVEMENT & SODDING	2 days	Thu 3/11/21	Sat 3/13/21	0%																												
74	6.32 SUBSTANCIAL COMPLETION	0 days	Sat 3/13/21	Sat 3/13/21	0%																												
75	7 CLOSEOUT ITEMS	19 days	Sat 3/13/21	Wed 3/31/21	0%																												
76	7.1 CLOSEOUT ALL PERMITS	6 days	Sat 3/13/21	Fri 3/19/21	0%																												
77	7.2 PERFORM WALK THROUGH FOR PUNCHLIST	1 day	Fri 3/19/21	Sat 3/20/21	0%																												
78	7.3 PERFORM PUNCHLIST ITEMS	7 days	Sat 3/20/21	Sat 3/27/21	0%																												
79	7.4 SUBMIT ALL REQUIRED CLOSEOUT DOCUMENTS, ASBUILTS, MANUALS, WARRANTIES,	5 days	Sat 3/27/21	Wed 3/31/21	0%																												
80	7.5 FINAL ACCEPTANCE	0 days	Wed 3/31/21	Wed 3/31/21	0%																												

30 days to get certification on 4/7/21

4/7/21

5/7/21 including 11 days contingency

