## DRAFT

### COASTAL RESILIENCY PHASE IV UNDERGROUNDING OF OVERHEAD UTILITIES AND STREETSCAPE PROJECT

#### PROJECT LOCATION



#### PROJECT STATUS

#### **PROEJCT STATUS:**

- All storm drainage work and tie-ins to the FDOT drainage system have been completed on every street.
- Conduit installation for the undergrounding of franchise utilities on the side streets is about 90% completed.
- Conduit tie-ins and installation of handholes is ongoing on the sidestreets.
- Directional drilling has begun on A1A for the undergrounding of franchise utilities. Currently working from Van Buren to Monroe.
- Streetscape construction has begun on Van Buren Street. We've completed the north sidewalk and are currently working on the south sidewalk. Roadway construction will begin after the south sidewalk is finished.


#### PROJECT SCHEDULE

#### PROJECT SCHEDULE:

#### **VAN BUREN STREET:**

- Sidewalk Subgrade South Side 9/25/2025 9/29/2025
- Paver installation south sidewalk 9/25/2025 9/30/2025
- Roadway Construction to begin on 10/1/2025. Starting 10/1/2025 the entire roadway will be closed to vehicle traffic. Anticipate roadway construction to be 4-5 weeks depending on the weather.

#### STORM DRAINAGE INSTALLATION

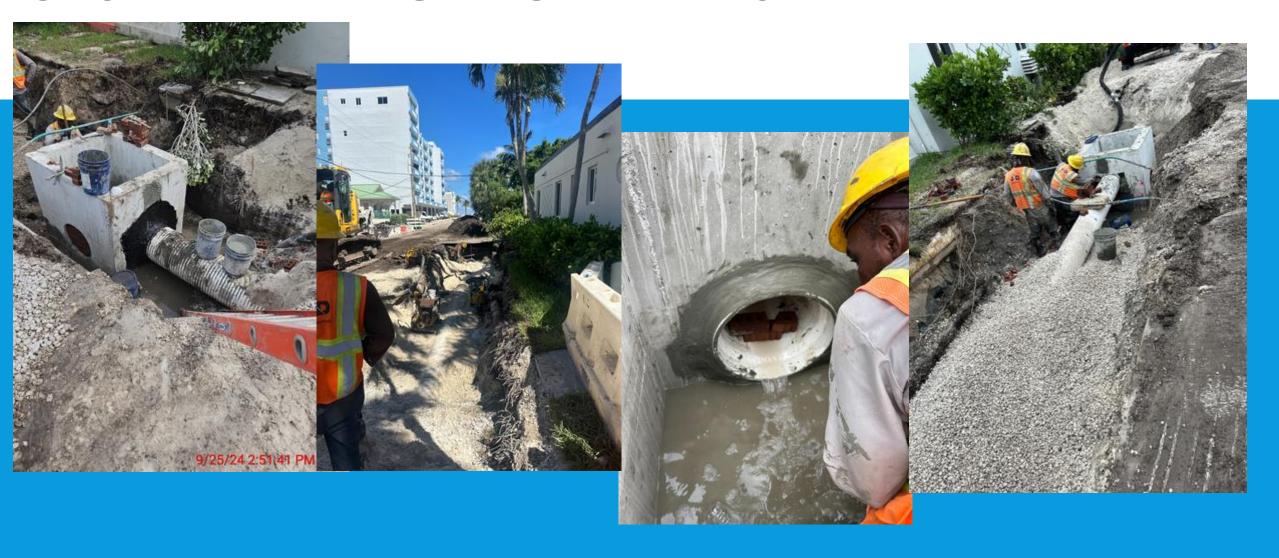

#### STORM DRAINAGE INSTALLATION








#### RESIDENT OUTREACH AND COORDINATION

- Resident outreach and coordination is ongoing throughout the project.
- BCI coordinates with the individual properties before we start work in front of them.
- BCI provides weekly/two week look aheads for the streets that are going to be impacted.
- BCI runs all communication through the CRA office and in conjunction with the CRA's community liaison.
- Community liaison contact: Melissa Rodriguez, Senior Community Outreach Specialist with HML Public Outreach. Cell: 305-570-8076. Email:melissa@hmlpublicoutreach.com

## FDOT PUMP CONSTRUCTION ALONG BEACH CRA BOUNDARIES

# LOCATION MAP CONSTRUCTION OF 3 PUMP STATIONS IN CRA BOUNDARIES

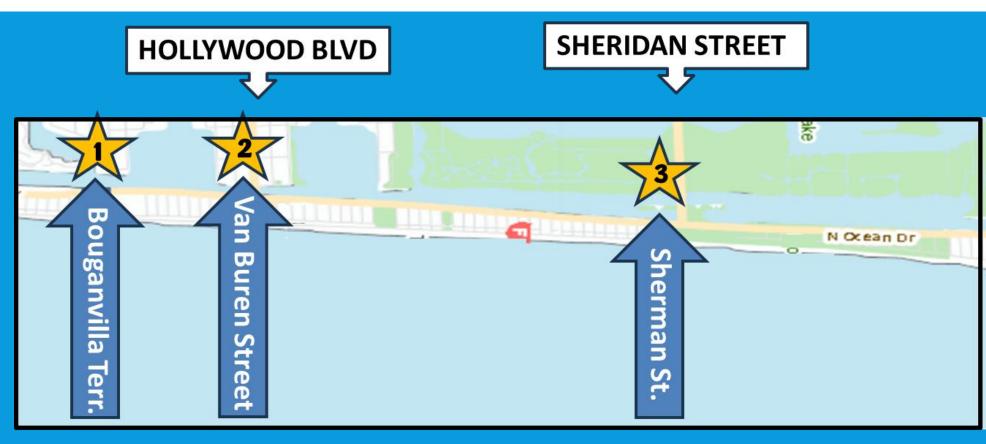

#### CRA COST CONTRICBUTION TO FDOT

Resolution	Scope	FM Number	Location	Amount
CRA 2024-14	Design	448574.1	Sherman St.	\$ 108,924.00
CRA 2024-14	Desing	448577.1	Van Buren/Bouganvilla	\$ 469,839.00
CRA 2024-14	Construction	448574.1	Sherman St.	\$ 878,059.83
CRA 2024-14	Construction	448577.1	Van Buren/Bouganvilla	\$ 3,916,705.97
TOTAL				\$ 5,373,528.80

#### PROJECT STATUS

Fj-Group to provide status and project

#### PROJECT SCHEDULE

Fj-Group to provide project schedule

## QUESTIONS
