


Stan Goldman Skatepark - Hollywood, FL

ID	Task Mode	Task Name	Duration	Start	Finish	4th Quarter		1st Quarter			2nd Quarter			3rd Quarter		
						Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
1		Stan Goldman Skatepark	168 days	Mon 11/11/24	Wed 7/2/25											
2		Storm Water Report - Engineering	15 days	Mon 11/11/24	Fri 11/29/24											
3		County Permit Process	45 days	Mon 12/2/24	Fri 1/31/25											
4		City Permit Process	5 days	Mon 2/3/25	Fri 2/7/25											
5		Mobilization	2 days	Wed 2/12/25	Thu 2/13/25											
6		Installation of BMP's	5 days	Wed 2/12/25	Tue 2/18/25											
7		Demolition of Existing Asphalt Pad	3 days	Wed 2/19/25	Fri 2/21/25											
8		Site Staking & Layout	5 days	Mon 2/24/25	Fri 2/28/25											
9		Rough Grading of Park	15 days	Wed 2/26/25	Tue 3/18/25											
10		Form and Metal of Features	30 days	Wed 3/19/25	Tue 4/29/25											
11		Rebar & Shoot Specialty Features	20 days	Wed 5/14/25	Tue 6/10/25											
12		Rebar & Pour Ledges/Stairs	10 days	Wed 4/16/25	Tue 4/29/25											
13		Form, Rebar and Pour Flatwork	10 days	Wed 6/11/25	Tue 6/24/25											
14		Fine Grading	6 days	Wed 6/18/25	Wed 6/25/25											
15		Painting, Caulking, Clean Up Punch	5 days	Thu 6/26/25	Wed 7/2/25											

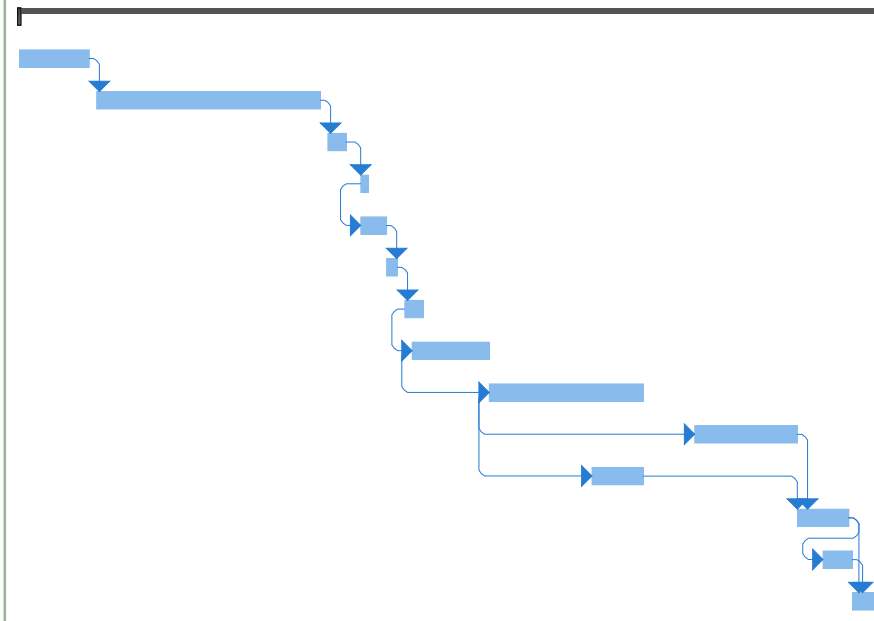

Project: 11.07.24 Revised Project
Date: Thu 11/7/24

Task		Inactive Task		Manual Summary Rollup		External Milestone	
Split		Inactive Milestone		Manual Summary		Deadline	
Milestone		Inactive Summary		Start-only		Progress	
Summary		Manual Task		Finish-only		Manual Progress	
Project Summary		Duration-only		External Tasks			

*This schedule is dependent on permitting turnaround and could change.
