


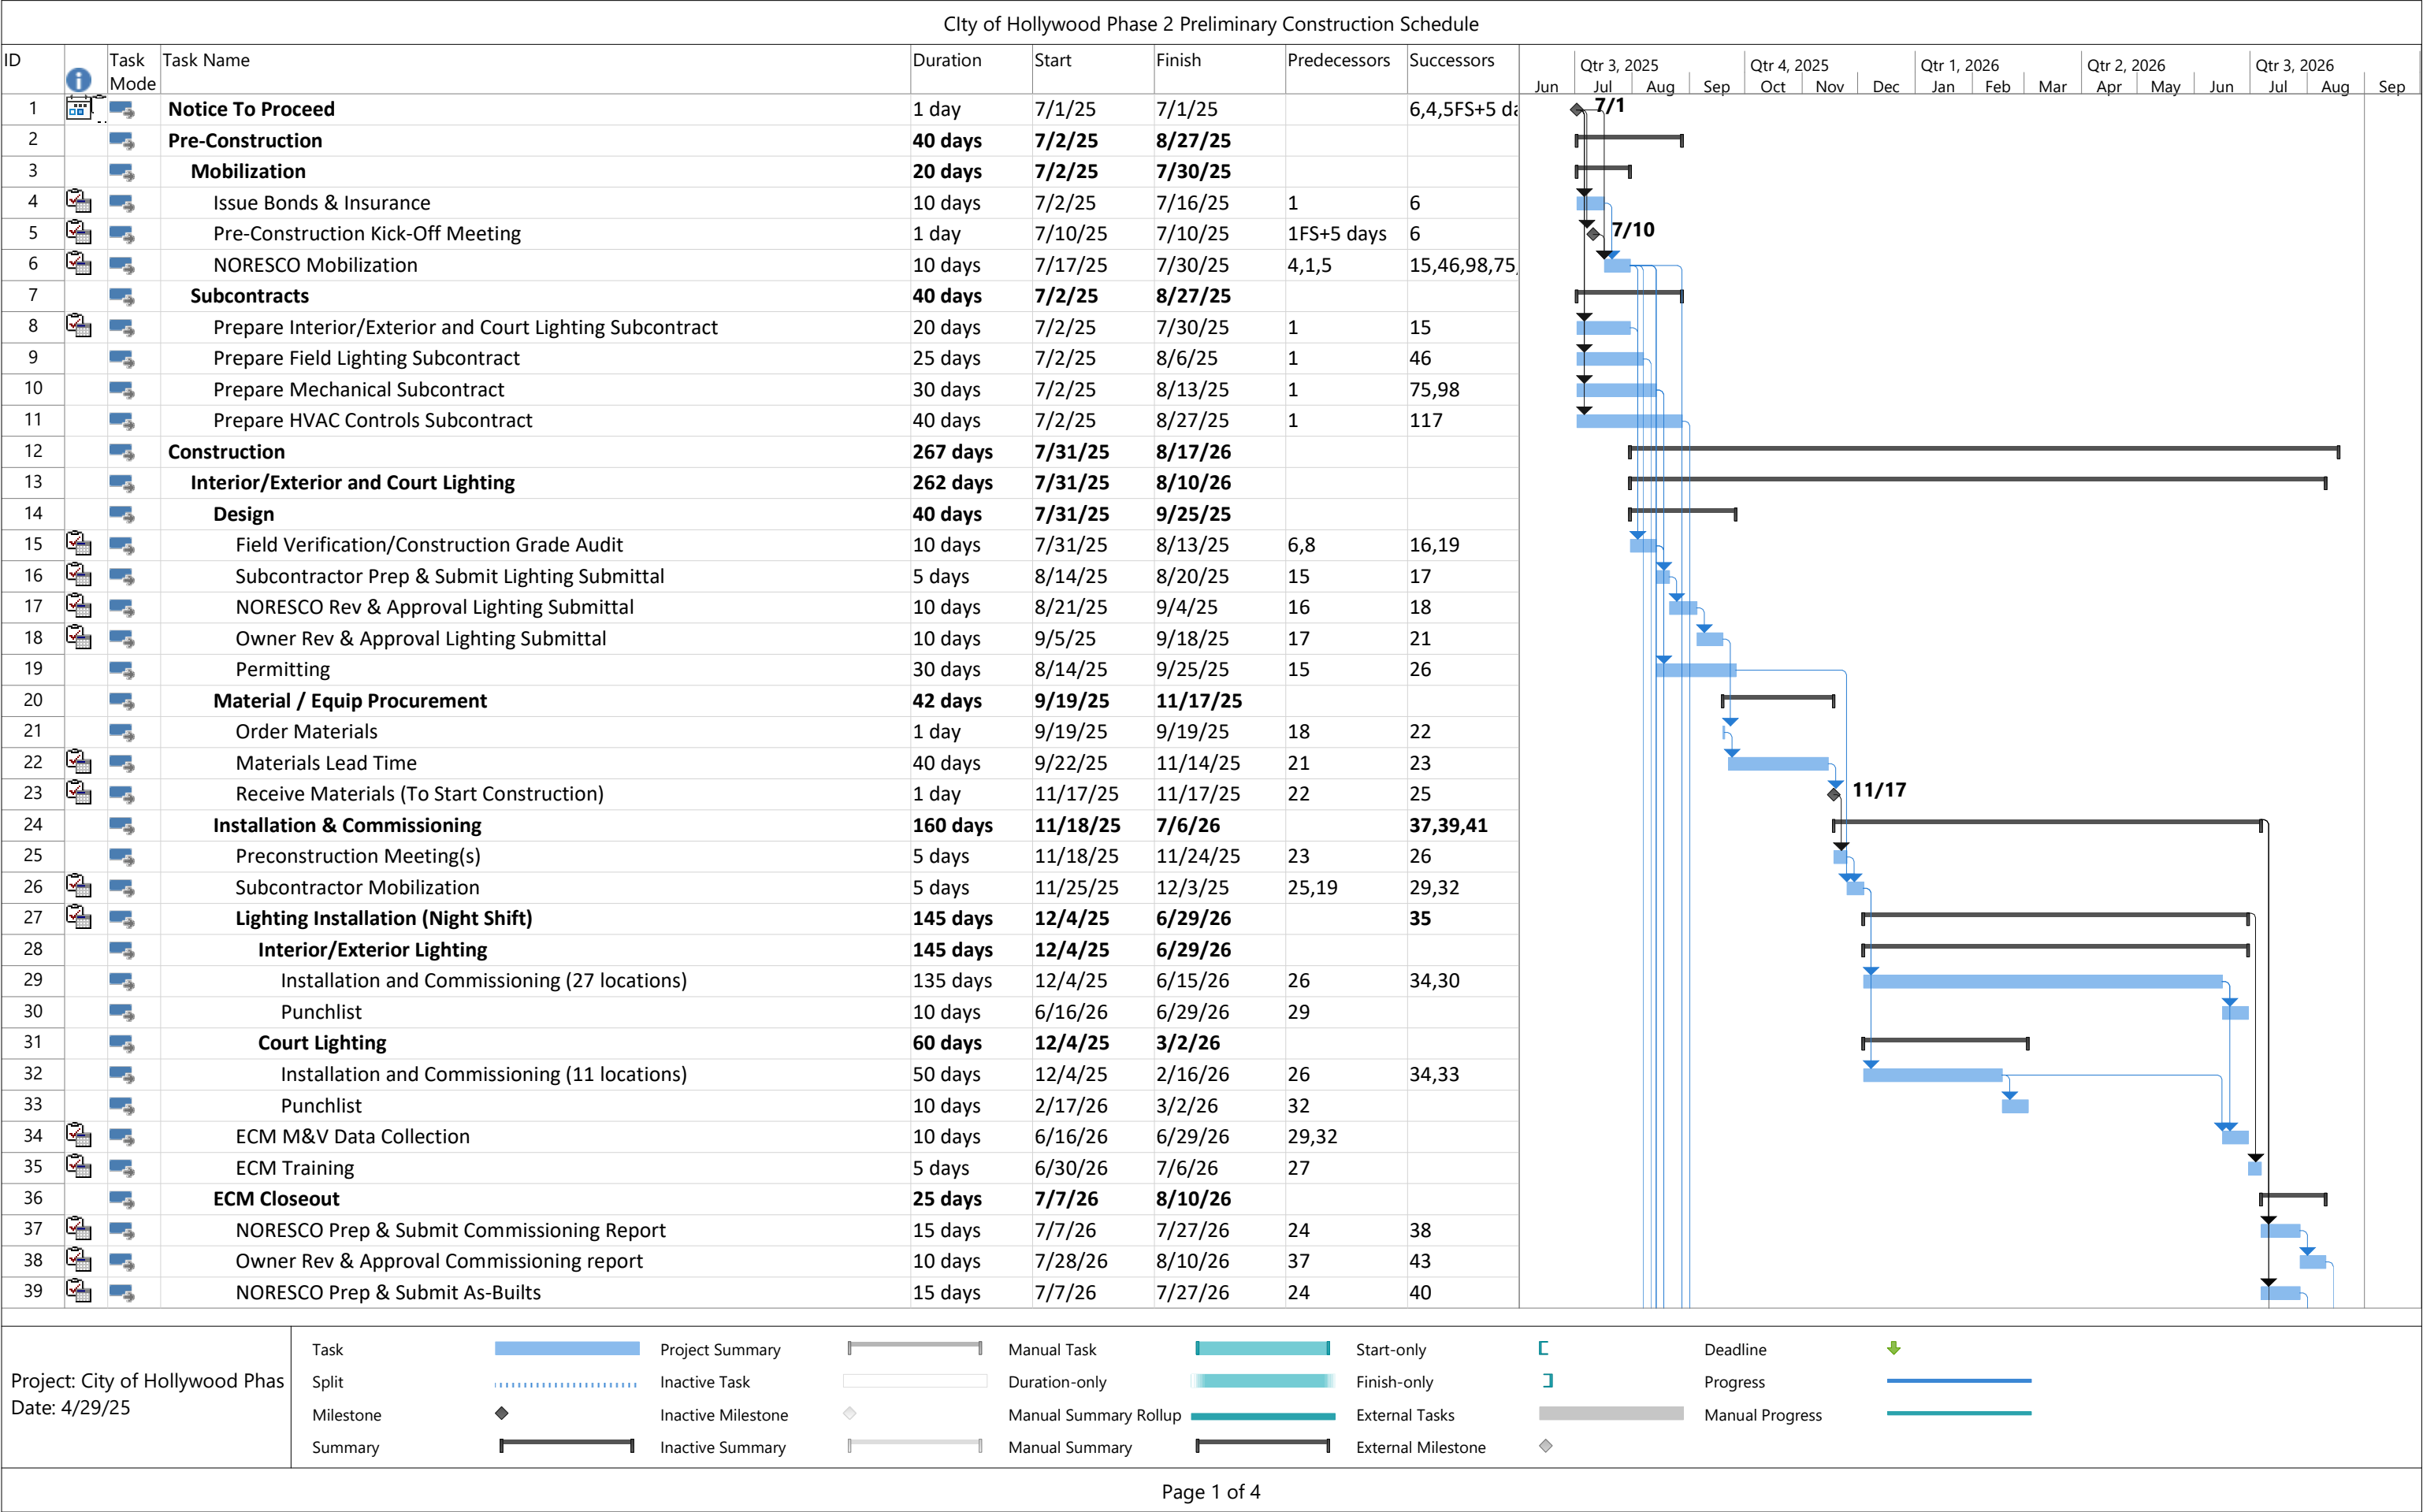

City of Hollywood Phase 2 Preliminary Construction Schedule																																
ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors																								
									Jun	Qtr 3, 2025				Qtr 4, 2025			Qtr 1, 2026			Qtr 2, 2026			Qtr 3, 2026									
									Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep									
40			Owner Rev & Approve As-Builts	10 days	7/28/26	8/10/26	39	43																								
41			NORESCO Prep & Submit Training & O+M Manuals	15 days	7/7/26	7/27/26	24	42																								
42			Owner Rev & Approve Training & O+M Manuals	10 days	7/28/26	8/10/26	41	43																								
43			Owner Approval ECM Completion	0 days	8/10/26	8/10/26	38,40,42	141																								
44			Field Lighting	262 days	8/7/25	8/17/26																										
45			Design	40 days	8/7/25	10/2/25		52																								
46			Field Verification	10 days	8/7/25	8/20/25	6,9	47,50																								
47			Subcontractor Prep & Submit Field Lighting Submittal	10 days	8/21/25	9/4/25	46	48																								
48			NORESCO Rev & Approval Field Lighting Submittal	10 days	9/5/25	9/18/25	47	49																								
49			Owner Rev & Approval Field Lighting Submittal	10 days	9/19/25	10/2/25	48																									
50			Permitting	30 days	8/21/25	10/2/25	46	56																								
51			Material / Equip Procurement	62 days	10/3/25	1/5/26																										
52			Order Materials	1 day	10/3/25	10/3/25	45	53																								
53			Materials Lead Time	60 days	10/6/25	1/2/26	52	54																								
54			Receive Materials (To Start Construction)	1 day	1/5/26	1/5/26	53	56																								
55			Installation & Commissioning	140 days	1/6/26	7/20/26		67,69																								
56			Subcontractor Mobilization	5 days	1/6/26	1/12/26	54,50	58,60																								
57			Field Lighting	125 days	1/13/26	7/6/26																										
58			Hollywood West Sports Lighting	30 days	1/13/26	2/23/26	56	59,63,64																								
59			Police Athletic Leage (Boggs East and West Parks)	50 days	2/24/26	5/4/26	58	63,64																								
60			Driftwood Park	30 days	1/13/26	2/23/26	56	61,63,64																								
61			Washington Park Sports Lighting	35 days	2/24/26	4/13/26	60	63,62,64																								
62			Rotary Park	50 days	4/14/26	6/22/26	61	63,64																								
63			Punchlist	10 days	6/23/26	7/6/26	61,58,59,60,66	65																								
64			ECM M&V Data Collection	10 days	6/23/26	7/6/26	58,59,60,61,66																									
65			ECM Training	10 days	7/7/26	7/20/26	63																									
66			ECM Closeout	20 days	7/21/26	8/17/26																										
67			NORESCO Prep & Submit As-Builts	10 days	7/21/26	8/3/26	55	68																								
68			Owner Rev & Approve As-Builts	10 days	8/4/26	8/17/26	67	71																								
69			NORESCO Prep & Submit Training & O+M Manuals	10 days	7/21/26	8/3/26	55	70																								
70			Owner Rev & Approve Training & O+M Manuals	10 days	8/4/26	8/17/26	69	71																								
71			Owner Approval ECM Completion	0 days	8/17/26	8/17/26	68,70	141																								
72			Mechanical and Controls	202 days	8/14/25	6/1/26																										
73			Mechanical (David Park CC)	172 days	8/14/25	4/20/26																										
74			Design	111 days	8/14/25	1/23/26																										
75			Field Verification Site Visits	10 days	8/14/25	8/27/25	10,6	76																								
76			75% Design Prep	15 days	8/28/25	9/18/25	75	77																								
77			75% Design NORESKO Review	10 days	9/19/25	10/2/25	76	78																								
78			95% Design Prep	10 days	10/3/25	10/16/25	77	79																								

Project: City of Hollywood Phas

Date: 4/29/25

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 2 of 4

[illegible]

City of Hollywood Phase 2 Preliminary Construction Schedule																									
ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Successors																	
									Jun	Qtr 3, 2025			Qtr 4, 2025			Qtr 1, 2026			Qtr 2, 2026			Qtr 3, 2026			
										Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	
118			Subcontractor Prep & Submit Controls Equipment Submittal	10 days	9/5/25	9/18/25	117	119																	
119			NORESCO Rev & Approve Controls Equipment Submittal	10 days	9/19/25	10/2/25	118	120																	
120			Owner Rev & Approve Controls Equipment Submittal	10 days	10/3/25	10/16/25	119	122																	
121			Equipment Procurement	22 days	10/17/25	11/17/25																			
122			Order Equipment	1 day	10/17/25	10/17/25	120	123																	
123			Controls Equipment Lead Time	20 days	10/20/25	11/14/25	122	124																	
124			Receive Equipment (To Start Construction)	1 day	11/17/25	11/17/25	123	126																	
125			Installation & Commissioning	50 days	11/18/25	2/2/26		133,135,137																	
126			Subcontractor Mobilization	5 days	11/18/25	11/24/25	124	128																	
127			Controls Installation	45 days	11/25/25	2/2/26																			
128			City Wide	35 days	11/25/25	1/19/26	126	129FF																	
129			Commissioning	10 days	1/6/26	1/19/26	128FF	130																	
130			Punchlist	5 days	1/20/26	1/26/26	129	131																	
131			ECM Training	5 days	1/27/26	2/2/26	130																		
132			ECM Closeout	20 days	5/5/26	6/1/26																			
133			NORESCO Prep & Submit Commissioning Report	10 days	5/5/26	5/18/26	107,125	134																	
134			Owner Rev & Approval Commissioning report	10 days	5/19/26	6/1/26	133	139																	
135			NORESCO Prep & Submit As-Builts	10 days	5/5/26	5/18/26	107,125	136																	
136			Owner Rev & Approval As-Builts	10 days	5/19/26	6/1/26	135	139																	
137			NORESCO Prep & Submit Training & O+M Manuals	10 days	5/5/26	5/18/26	107,125	138																	
138			Owner Rev & Approval Training & O+M Manuals	10 days	5/19/26	6/1/26	137	139																	
139			Owner Approval ECM Completion	0 days	6/1/26	6/1/26	134,136,138	141																	
140			Project Closeout	20 days	8/4/26	8/31/26		145																	
141			All ECM's Completed	0 days	8/17/26	8/17/26	43,139,71	143FF,142FF																	
142			Project Demobilization	10 days	8/4/26	8/17/26	141FF																		
143			NORESCO Prep & Submit Project Close-out Documents	10 days	8/4/26	8/17/26	141FF	144																	
144			Owner Rev & Approve Project Close-out Docs	10 days	8/18/26	8/31/26	143																		
145			Project Final Acceptance	0 days	8/31/26	8/31/26	140																		
Project: City of Hollywood Phas Date: 4/29/25			Task		Project Summary		Manual Task		Start-only		Deadline														
			Split		Inactive Task		Duration-only		Finish-only		Progress														
			Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress														
			Summary		Inactive Summary		Manual Summary		External Milestone																
Page 4 of 4																									
