

Exhibit C

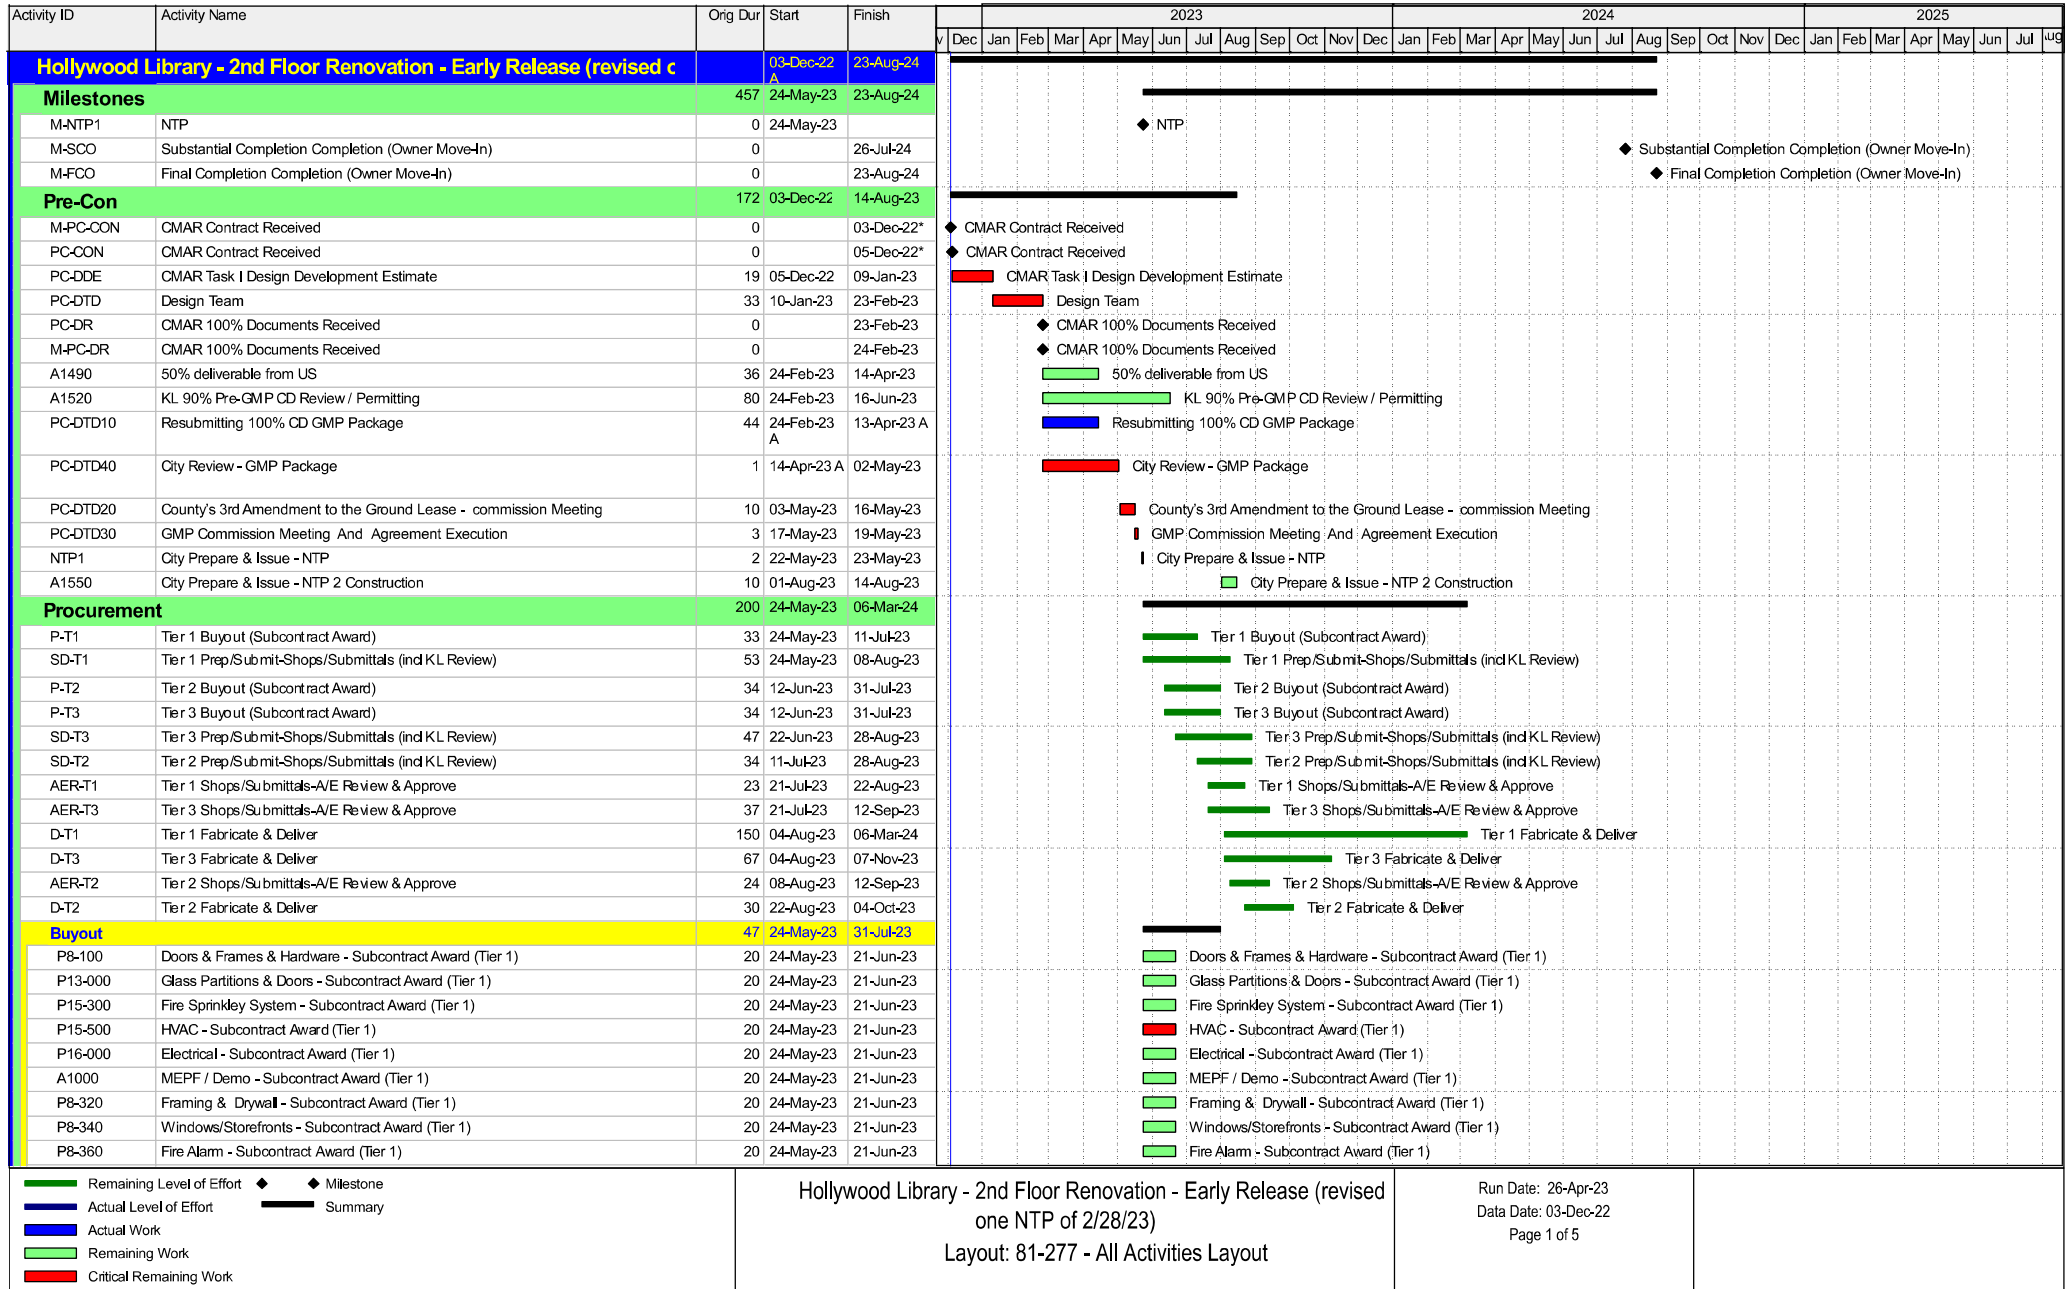


Exhibit C

Activity ID	Activity Name	Orig Dur	Start	Finish	2023												2024												2025											
					Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug			
SDS11-465	Kitchen Equipment - Prep & Submit (ind KL Review) (Tier 3)	20	01-Aug-23	28-Aug-23	Kitchen Equipment - Prep & Submit (ind KL Review) (Tier 3)																																			
AE Review & Approve					37 21-Jul-23 12-Sep-23																																			
AER8-100	Doors & Frames - Shops/Submittals-A/E Review & Approve (Tier 3)	10	21-Jul-23	03-Aug-23	Doors & Frames - Shops/Submittals-A/E Review & Approve (Tier 3)																																			
AER13-000	Glass Partitions & Doors - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	Glass Partitions & Doors - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER15-300	Fire Sprinkley System - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	Fire Sprinkley System - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER15-500	HVAC - AHU - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	HVAC - AHU - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER16-000	Electrical Lighting - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	Electrical Lighting - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER15-510	HVAC - VAV - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	HVAC - VAV - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER15-520	HVAC - Controls - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	HVAC - Controls - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER15-530	HVAC - Split System - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	HVAC - Split System - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER15-540	HVAC - Fans / Louvers - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	HVAC - Fans / Louvers - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER15-550	HVAC - Duct Work - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	HVAC - Duct Work - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER16-10	Electrical Switchgear - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	Electrical Switchgear - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER16-20	Electrical Conduit & Wire - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	Electrical Conduit & Wire - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER16-30	Electrical Cable Tray - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	Electrical Cable Tray - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER15-310	Fire Alarm - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	Fire Alarm - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER16-50	Framing & Drywall - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	Framing & Drywall - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER16-60	Windows/Storefronts - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	Windows/Storefronts - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER16-70	Millwork - Shops/Submittals-A/E Review & Approve (Tier 1)	10	21-Jul-23	03-Aug-23	Millwork - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER9-050	Metal Framing - Shops/Submittals-A/E Review & Approve (Tier 2)	10	08-Aug-23	22-Aug-23	Metal Framing - Shops/Submittals-A/E Review & Approve (Tier 2)																																			
AER9-500	Acoustical Ceilings - Shops/Submittals-A/E Review & Approve (Tier 2)	10	08-Aug-23	22-Aug-23	Acoustical Ceilings - Shops/Submittals-A/E Review & Approve (Tier 2)																																			
AER9-300	Flooring - Shops/Submittals-A/E Review & Approve (Tier 2)	10	08-Aug-23	22-Aug-23	Flooring - Shops/Submittals-A/E Review & Approve (Tier 2)																																			
AER9-900	Painting - Shops/Submittals-A/E Review & Approve (Tier 3)	10	08-Aug-23	22-Aug-23	Painting - Shops/Submittals-A/E Review & Approve (Tier 3)																																			
AER15-400	Plumbing Piping & Fittings - Shops/Submittals-A/E Review & Approve (Tier 1)	10	08-Aug-23	22-Aug-23	Plumbing Piping & Fittings - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER15-410	Plumbing Fixtures - Shops/Submittals-A/E Review & Approve (Tier 1)	10	08-Aug-23	22-Aug-23	Plumbing Fixtures - Shops/Submittals-A/E Review & Approve (Tier 1)																																			
AER16-80	Waterproofing - Shops/Submittals-A/E Review & Approve (Tier 2)	10	08-Aug-23	22-Aug-23	Waterproofing - Shops/Submittals-A/E Review & Approve (Tier 2)																																			
AER3-350	Concrete - Shops/Submittals-A/E Review & Approve (Tier 3)	10	29-Aug-23	12-Sep-23	Concrete - Shops/Submittals-A/E Review & Approve (Tier 3)																																			
AER5-010	Metals - Shops/Submittals-A/E Review & Approve (Tier 3)	10	29-Aug-23	12-Sep-23	Metals - Shops/Submittals-A/E Review & Approve (Tier 3)																																			
AER6-400	Wood, Plastics & Composites - Shops/Submittals-A/E Review & Approve (Tier 3)	10	29-Aug-23	12-Sep-23	Wood, Plastics & Composites - Shops/Submittals-A/E Review & Approve (Tier 3)																																			
AER8-400	Window Replacement - Shops/Submittals-A/E Review & Approve (Tier 3)	10	29-Aug-23	12-Sep-23	Window Replacement - Shops/Submittals-A/E Review & Approve (Tier 3)																																			
AER9-200	Stucco - Shops/Submittals-A/E Review & Approve (Tier 3)	10	29-Aug-23	12-Sep-23	Stucco - Shops/Submittals-A/E Review & Approve (Tier 3)																																			
AER10-500	Specialties - Shops/Submittals-A/E Review & Approve (Tier 3)	10	29-Aug-23	12-Sep-23	Specialties - Shops/Submittals-A/E Review & Approve (Tier 3)																																			
AER11-465	Kitchen Equipment - Shops/Submittals-A/E Review & Approve (Tier 3)	10	29-Aug-23	12-Sep-23	Kitchen Equipment - Shops/Submittals-A/E Review & Approve (Tier 3)																																			
Fabricate & Deliver					150 04-Aug-23 06-Mar-24																																			
D8-100	Doors & Frames -Fabricate & Deliver (Tier 3)	30	04-Aug-23	15-Sep-23	Doors & Frames -Fabricate & Deliver (Tier 3)																																			
D13-000	Glass Partitions & Doors -Fabricate & Deliver (Tier 1)	40	04-Aug-23	29-Sep-23	Glass Partitions & Doors -Fabricate & Deliver (Tier 1)																																			
D15-300	Fire Sprinkley System -Fabricate & Deliver (Tier 1)	30	04-Aug-23	15-Sep-23	Fire Sprinkley System -Fabricate & Deliver (Tier 1)																																			
D15-500	HVAC - AHU -Fabricate & Deliver (Tier 1)	150	04-Aug-23	06-Mar-24	HVAC - AHU -Fabricate & Deliver (Tier 1)																																			
D16-000	Lighting -Fabricate & Deliver (Tier 1)	60	04-Aug-23	27-Oct-23	Lighting -Fabricate & Deliver (Tier 1)																																			
D15-510	HVAC - VAV -Fabricate & Deliver (Tier 1)	60	04-Aug-23	27-Oct-23	HVAC - VAV -Fabricate & Deliver (Tier 1)																																			
D15-520	HVAC - Controls -Fabricate & Deliver (Tier 1)	40	04-Aug-23	29-Sep-23	HVAC - Controls -Fabricate & Deliver (Tier 1)																																			
D15-530	HVAC - Split System -Fabricate & Deliver (Tier 1)	30	04-Aug-23	15-Sep-23	HVAC - Split System -Fabricate & Deliver (Tier 1)																																			
D15-540	HVAC - Fans Louvers -Fabricate & Deliver (Tier 1)	40	04-Aug-23	29-Sep-23	HVAC - Fans Louvers -Fabricate & Deliver (Tier 1)																																			
D15-550	HVAC - Duct Work -Fabricate & Deliver (Tier 1)	15	04-Aug-23	24-Aug-23	HVAC - Duct Work -Fabricate & Deliver (Tier 1)																																			
D16-10	Electrical Switchgear / ATS / Transformer Fabricate & Deliver	125	04-Aug-23	31-Jan-24	Electrical Switchgear / ATS / Transformer Fabricate & Deliver																																			

■ Remaining Level of Effort ◆ Milestone
■ Actual Level of Effort — Summary
■ Actual Work
■ Remaining Work
■ Critical Remaining Work

Hollywood Library - 2nd Floor Renovation - Early Release (revised one NTP of 2/28/23)
 Layout: 81-277 - All Activities Layout

Run Date: 26-Apr-23
 Data Date: 03-Dec-22
 Page 3 of 5

Exhibit C



Kaufman Lynn Construction, Inc.

Job #: 81-277 Hollywood - BC 2nd Floor Library
City Hall
Hollywood, Florida 33020

Current Drawings

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
Architectural					
A-100	GENERAL NOTES	2	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
A-101	PROPOSED FLOOR PLAN AND NOTES	3	09/14/2022		Bldg. Dept. Comments 09_14_2022
A-102	POWER LOCATION PLAN AND NOTES	2	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
A-103	POWER DETAILS AND SCHEDULE	2	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
A-301	ENLARGED RESTROOM PLAN AND ELEVATIONS	2	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
A-302	ENLARGED RESTROOM PLAN AND ELEVATIONS	2	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
A-303	ENLARGED PLANS AND ELEVATIONS	1	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
A-304	ENLARGED PLANS AND ELEVATIONS	1	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
A-305	ENLARGED PLANS AND ELEVATIONS	3	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
A-401	REFLECTED CEILING PLAN AND NOTES	2	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
A-402	REFLECTED CEILING DETAILS	2	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
A-501	TYPICAL FIRE PENETRATION DETAILS	2	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
A-701	WALL TYPES	3	09/14/2022		Bldg. Dept. Comments 09_14_2022
A-801	DOOR & WINDOW SCHEDULES	3	09/14/2022		Bldg. Dept. Comments 09_14_2022
A-901	PROPOSED FLOOR FINISH PLAN AND NOTES	2	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
A-902	FINISH SCHEDULE	2	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
Cover					
T-001	COVER SHEET	3	09/14/2022		Bldg. Dept. Comments 09_14_2022
Demolition					
D-101	DEMOLITION PLAN AND NOTES	2	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
Electrical					
E-100	INDEX, SYMBOL LEGEND, AND NOTES	5	09/06/2022		Bldg. Dept. Comments 09_06_2022
E-101	PROPOSED FLOOR PLAN - POWER	5	09/06/2022		Bldg. Dept. Comments 09_06_2022

Exhibit C



Kaufman Lynn Construction, Inc.

Job #: 81-277 Hollywood - BC 2nd Floor Library
City Hall
Hollywood, Florida 33020

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
E-102	PROPOSED FLOOR PLAN - POWER	5	09/06/2022		Bldg. Dept. Comments 09_06_2022
E-103	PROPOSED FLOOR PLAN - LIGHTING	5	09/06/2022		Bldg. Dept. Comments 09_06_2022
E-104	PROPOSED FLOOR PLAN - LIGHTING	4	09/06/2022		Bldg. Dept. Comments 09_06_2022
E-200	RISER DIAGRAM	5	09/06/2022		Bldg. Dept. Comments 09_06_2022
E-201	PANEL SCHEDULES	5	09/06/2022		Bldg. Dept. Comments 09_06_2022
Fire Alarm					
FA-100	INDEX, SYMBOL LEGEND, AND NOTES	4	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
FA-101	PROPOSED FLOOR PLAN - FIRE ALARM	4	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
FA-102	PROPOSED FLOOR PLAN - FIRE ALARM	5	09/06/2022		Bldg. Dept. Comments 09_06_2022
Fire Protection					
FP-100	FIRE PROTECTION INDEX, SYMBOL LEGEND AND NOTES	4	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
FP-101a	PROPOSED FIRE PROTECTION PLAN	4	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
FP-101b	PROPOSED FIRE PROTECTION PLAN	4	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
Life Safety					
LS-101	LIFE SAFETY PLAN	3	09/14/2022		Bldg. Dept. Comments 09_14_2022
Mechanical					
M-100	INDEX, SYMBOL LEGEND, AND NOTES	3	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
M-102a	PROPOSED FLOOR PLAN - MECHANICAL	5	09/06/2022		Bldg. Dept. Comments 09_06_2022
M-102b	PROPOSED FLOOR PLAN - MECHANICAL	5	09/06/2022		Bldg. Dept. Comments 09_06_2022
M-200	MECHANICAL SCHEDULES	3	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
M-300	MECHANICAL DETAILS	2	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
M-301	MECHANICAL DETAILS	1	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
M-400	INDEX, SYMBOL LEGEND, AND NOTES	3	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
Plumbing					
P-100	INDEX, SYMBOL LEGEND AND NOTES	3	08/10/2022		100% CD - Permit Set 08_10_2022 (08/10/22)
P-101	PROPOSED FLOOR PLAN - DOMESTIC WATER	5	09/06/2022		Bldg. Dept. Comments 09_06_2022
P-102	PROPOSED FLOOR PLAN - DOMESTIC WATER	5	09/06/2022		Bldg. Dept. Comments 09_06_2022
P-103	PROPOSED FLOOR PLAN - SANITARY	5	09/06/2022		Bldg. Dept. Comments 09_06_2022
P-104	PROPOSED FLOOR PLAN - SANITARY	5	09/06/2022		Bldg. Dept. Comments 09_06_2022
P-200	ISOMETRICS	2	09/06/2022		Bldg. Dept. Comments 09_06_2022



Kaufman Lynn Construction, Inc.

Job #: 81-277 Hollywood - BC 2nd Floor Library
 City Hall
 Hollywood, Florida 33020

Current Specifications

Number	Description	Revision	Issued Date	Received Date	Set
00 - Procurement and Contracting Requirements					
000110	Table of Contents	0	08/11/22		Project Manual 08/11/2022
01 - General Requirements					
01332	Shop Drawings, Product Data, and Samples	0	08/11/22		Project Manual 08/11/2022
01354	Construction Indoor Air Quality Management	0	08/11/22		Project Manual 08/11/2022
01572	Construction Waste Management	0	08/11/22		Project Manual 08/11/2022
05 - Metals					
05400	Cold Formed Metal Framing	0	08/11/22		Project Manual 08/11/2022
06 - Wood, Plastics, and Composites					
06100	Rough Carpentry	0	08/11/22		Project Manual 08/11/2022
06300	Wood Treatment	0	08/11/22		Project Manual 08/11/2022
06400	Architectural Woodwork	0	08/11/22		Project Manual 08/11/2022
07 - Thermal and Moisture Protection					
07210	Building Insulation	0	08/11/22		Project Manual 08/11/2022
07920	Joint Sealers	0	08/11/22		Project Manual 08/11/2022
08 - Openings					
08110	Steel Doors and Frames	0	08/11/22		Project Manual 08/11/2022
08210	Flush Wood Doors	0	08/11/22		Project Manual 08/11/2022
08305	Access Doors and Panels	0	08/11/22		Project Manual 08/11/2022
08400	Entrances and Storefronts	0	08/11/22		Project Manual 08/11/2022
08710	Door Hardware	0	08/11/22		Project Manual 08/11/2022
08800	Glass and Glazing	0	08/11/22		Project Manual 08/11/2022
09 - Finishes					
09250	Gypsum Board	0	08/11/22		Project Manual 08/11/2022
09310	Ceramic and Porcelain Tile	0	08/11/22		Project Manual 08/11/2022
09510	Acoustical Ceilings	0	08/11/22		Project Manual 08/11/2022
09650	Resilient Flooring	0	08/11/22		Project Manual 08/11/2022
09683	Carpet Tile	0	08/11/22		Project Manual 08/11/2022
09720	Wall Covering	0	08/11/22		Project Manual 08/11/2022
09900	Painting	0	08/11/22		Project Manual 08/11/2022
10 - Specialties					
10211	Toilet Compartments	0	08/11/22		Project Manual 08/11/2022
10522	Fire Extinguishers, Cabinets, and Accessories	0	08/11/22		Project Manual 08/11/2022

Exhibit C



Kaufman Lynn Construction, Inc.

Job #: 81-277 Hollywood - BC 2nd Floor Library
City Hall
Hollywood, Florida 33020

Number	Description	Revision	Issued Date	Received Date	Set
10810	Toilet Accessories	0	08/11/22		Project Manual 08/11/2022
12 - Furnishings					
12366	Quartz	0	08/11/22		Project Manual 08/11/2022
12500	Window Treatments	0	08/11/22		Project Manual 08/11/2022
